

Weather

6:00 AM

42°

Windy and Partly Cloudy

Wind: 26 MPH | Precipitation: .06" | Humidity: 59%

12:00 PM

41°

Windy

Wind: 28 MPH | Precipitation: .07" | Humidity: 53%

4:00 PM

42°

Windy

Wind: 28 MPH | Precipitation: .07" | Humidity: 50%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0


General Notes

1. Mike and Jim onsite for Dellbrook ,
Today 6 carpenters working on both Buildings 3 at EMS finishing roof framing and prep for insulation and roof trim
3 working at FH on exterior insulation . I noticed that the Z channels were not being fastened according to Spec at FH . I sent Pics to Mike Leon and he came down and made sure that additional fasteners were being installed .

The masons wren cleaning up at FH getting ready to demobilize ,another Milestone for the job . Masons done .

Farland was trying to finish excavation and prep for trench drains at FH as of 3:30 they had not finished but will in the AM .
Electrician was working on FH interior wiring with 2 men .
Dellbrooks site safety officer Dan was onsite in the morning doing a walk around with Jim Watt making sure all safety protocols were being met

William Dillon | 12/01/22 | 05:10PM

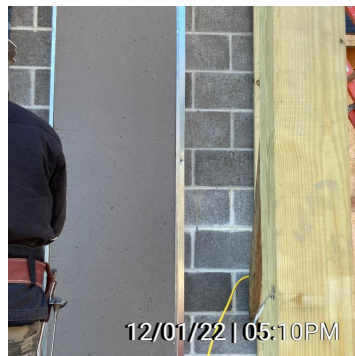

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Site Safety Officer form Dellbrook this morning William Dillon 12/01/22 05:11PM
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/01/22 | 05:11PM

Weather

6:00 AM

52° 

Rain

Wind: 20 MPH | Precipitation: .14" | Humidity: 90%

12:00 PM

53° 

Rain

Wind: 21 MPH | Precipitation: .45" | Humidity: 90%

4:00 PM

54° 

Rain

Wind: 18 MPH | Precipitation: .61" | Humidity: 93%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0


General Notes

1. Team Meeting this morning with Dellbrook team , Mike Owen ,Adity, Bill R, Allison K, Jeremy B, Tim C. John K's firm was represented by Antonia, and Jerry.
Mike Leon went over the next two weeks on the schedule.
The Silo is still being watched and the safety team is coming next week to do the next two tests on the tank connector and the tank its self.
There were 2 mason Laborers on site cleaning up and getting ready to leave job . This is a Milestone for the job.
There were 2 plumbers on site checking the Trench drains as steel was placed, then 2 plumbers were also working on plumbing rough in the FH.
The Garage doors at the FH were closed in to the weather yesterday .
Windows for the job arrived yesterday , Mike Leon expects to start setting them this week at the FH .
The temp heat is ready to start at the FH as soon as windows are Placed This will help dry out plywood roof and dry out the CMU.
In the meeting today it was noted that there have been no safety violations and only one small accident.
The Blueskin membrane has started on the FH which makes the walls watertight.

The exterior trim was discussed and there will still be a mockup , Mike O and I stressed the details must be followed for the exterior trim.

There were 6 men from Simmons Concrete setting up steel rebar , foam, and stage membrane in Apparatus bays of FH.
They will pour 2 of the 4 areas this week

William Dillon | 12/07/22 | 04:05PM

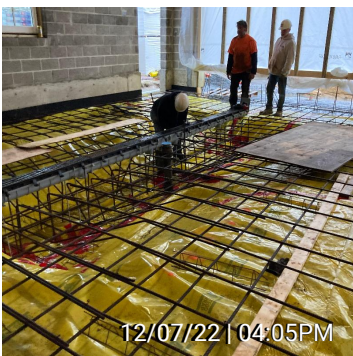

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Rain kept Carpenters away for the day William Dillon 12/07/22 04:06PM
4. Any visitors on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Dellbrook team and CHA William Dillon 12/07/22 04:07PM
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/07/22 | 04:07PM

Weather

6:00 AM

52° 

Partly Cloudy

Wind: 12 MPH | Precipitation: .01" | Humidity: 91%

12:00 PM

51° 

Clear

Wind: 17 MPH | Precipitation: .01" | Humidity: 83%

4:00 PM

49° 

Clear

Wind: 17 MPH | Precipitation: .01" | Humidity: 73%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- Today there were 13 Carpenters working at both sites 4 working at EMS putting insulation on roof and the remainder working at FH on exterior trim and odd and ends of interior blocking .
There were 2 plumbers working on copper piping in FH
Mike Leon was on site for Dellbrook , he and I talked about a big clean up before the Holiday week and Mike will get it done .
Mike hopes to get heat working in FH by mid week next week
Windows are on site and will be set by the end of next week at the FH .
One photo shows the Fireproofing in the 10' area near the Town Hall

William Dillon | 12/08/22 | 04:55PM



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
-----------	-----	----	-----	-------------

1. Any accidents on site today?

2. Any schedule delays occur?

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/08/22 | 04:58PM

Date Fri 12/09/2022

Job #

Prepared By William Dillon

Weather

6:00 AM

39° 

Clear

Wind: 20 MPH | Precipitation: .0" | Humidity: 75%

12:00 PM

45° 

Clear

Wind: 23 MPH | Precipitation: .0" | Humidity: 65%

4:00 PM

44° 

Windy

Wind: 26 MPH | Precipitation: .01" | Humidity: 55%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Jim Watt on site for Dellbrook .
13 Carpenters working on both sites . Roof Trim on FH partially done .
Jim moved all the Carpenters up to EMS to get roof water tight .
I asked Jim to clean up FH site before weekend and he had the Carpenters clean up .
As I walked around the FH I noticed that the joints in the Facia and Rakes was not done very well . I Told Jim that they were not acceptable and he said he will be on it and he will go back and fix .

William Dillon | 12/09/22 | 04:12PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/09/22 | 04:12PM

Weather

6:00 AM

39° 

Overcast

Wind: 25 MPH | Precipitation: .04" | Humidity: 88%

12:00 PM

35° 

Overcast

Wind: 25 MPH | Precipitation: .05" | Humidity: 80%

4:00 PM

34° 

Partly Cloudy

Wind: 23 MPH | Precipitation: .05" | Humidity: 68%

Work Logs


No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Today was busy on both sites . Mike Leon and Jim Watt onsite for Dellbrook.
There were 4 men from Simmons working on Slab prep at the FH .
There were two Plumbers working at the FH working on Copper piping .
There were 4 carpenters working at the EMS building starting the porches on the Yard side of the building ,and putting waterproofing on the EMS roof .
There were 4 carpenters working on Roof trim at the FH .
The Roofer started at the FH and by the end of the day they had done the entire Crossroads side of the FH two men working .
Friday I mentioned to Jim Watt that the exterior trim at the FH was not up to my standards , This morning I made sure that Mike Leon saw what I was talking about , Mike promised to fix , in one of the pictures I attached you can see daylight through the joint.

William Dillon | 12/12/22 | 05:35PM

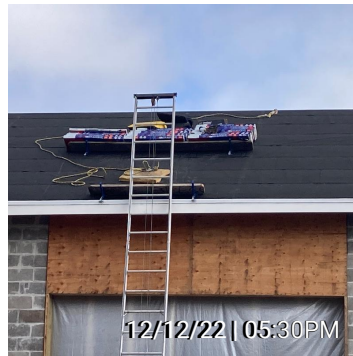

2. The Simmons crew was also installing Plastic over the window openings in preparation for getting temp heat .
Mike Leon also said that the window supplier will be onsite tomorrow to make sure windows are installed correctly

William Dillon | 12/12/22 | 05:32PM

Site Safety Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/12/22 | 05:33PM

Weather

6:00 AM

33° 

Clear

Wind: 15 MPH | Precipitation: .0" | Humidity: 66%

12:00 PM

38° 

Clear

Wind: 17 MPH | Precipitation: .0" | Humidity: 56%

4:00 PM

39° 

Clear

Wind: 19 MPH | Precipitation: .0" | Humidity: 49%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Mike L. and Jim W. in for Dellbrook.
The roofers were working on the FH today with 2 men
2 plumbers working on copper water piping and getting vents through the roof of FH .
1 Electrician working on duct bank coming out of FH.
3 Carpenters were working on exterior insulation at FH
4 Carpenters working on Porches and bracing at EMS
Structural Engineer was coming mid day to inspect all roof framing and hold downs at EMS
Farland excavation was working at FH cleaning up and getting ready for Tight Tanks at FH with 2 men .
Farland was also working at rear of FH prepping for more trenching for primary power

William Dillon | 12/13/22 | 05:55PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/13/22 | 05:55PM

Weather

6:00 AM

29° 

Windy

Wind: 28 MPH | Precipitation: .0" | Humidity: 64%

12:00 PM

34° 

Clear

Wind: 24 MPH | Precipitation: .0" | Humidity: 68%

4:00 PM

39° 

Clear

Wind: 23 MPH | Precipitation: .0" | Humidity: 65%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Team Meeting day , John Keenan , CHA team , Dellbrook team and Bill Rossi, Alison Kisselgof , Tim Carroll ,Jeremy Bradshaw.
Discussion regarding parking lot lighting , and snow guards for roof . Lighting has been decided . Snow guards being worked out by Craig Gabri .
There were 12 carpenters working on the EMS and FH today 9 on exterior trim ,and installing Blueskin and windows at the FH, 3 on siding details.
Farland was digging trenching for power and telecom at FH with 2 men .
The plumbers were working at FH installing water piping and roof vents .
There was discussion regarding a 2" water drop in the apprautus bay to top off fire trucks .
There were 2 electricians working at the FH on interior wiring and duct banks .
the 2 roofers finished as much as they could at the FH and moved up to start the EMS building .
The Carpenters were applying Blueskin cold weather adhesive before installing Blueskin which is what the specs say.
The Structural engineer was on site yesterday and said Mike Leon was doing a great job .
Mike Leon reported that the silo had only dropped 1/16" in the last week .He also reported that the tank safety team will be out next week to finalize tank testing .

William Dillon | 12/14/22 | 06:21PM



Site Safety Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/14/22 | 06:21PM

Weather

6:00 AM

41° 

Partly Cloudy

Wind: 18 MPH | Precipitation: .0" | Humidity: 81%

12:00 PM

44° 

Overcast

Wind: 16 MPH | Precipitation: .0" | Humidity: 85%

4:00 PM

44° 

Overcast

Wind: 18 MPH | Precipitation: .0" | Humidity: 85%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- very busy day at site .
18 Carpenters working at both sites , working setting windows and getting EMS roof tight .
The 2 roofers were working on the front of the EMS and prepping the back areas of the EMS
2 electricians were working at the FH getting more conduit into ground as Farland trenched .
Farland had 2 men onsite .
The 2 plumbers continued working on the FH plumbing .
Mile Leon had a meeting with Cara Semeth from Con Com regarding the trench and culvert at the TH entrance , Mike also met Eversource onsite ,
This was to schedule pole reinforcement when the trench work is done . That will happen Jan 6th
Tomorrow the site will be shut down

William Dillon | 12/15/22 | 05:32PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/15/22 | 05:33PM

Chilmark Fire House and EMS Building

Self

399 Middle Road Chilmark, Massachusetts 02535

Date Mon 12/19/2022

Job #

Prepared By William Dillon



Weather

6:00 AM

35° 

Clear

Wind: 22 MPH | Precipitation: .0" | Humidity: 75%

12:00 PM

39° 

Clear

Wind: 23 MPH | Precipitation: .0" | Humidity: 68%

4:00 PM

40° 

Clear

Wind: 24 MPH | Precipitation: .0" | Humidity: 64%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- Today there were 18 Carpenters on site split between EMS and FH . I had a long discussion with Mike and the Carpenters about trim around windows . The Carpenters were not glueing the trim joints so I made them remove trim re make the trim properly using glue as designed . The two electricians were prepping for the duct bank at the entrance to the TH parking lot . Farland was onsite working at the FH digging trench and excavation for structure for power and telecom . I spoke to the 2 plumbers working at the FH and they estimate that they are approximately 60% done with the Rough plumbing at the FH The slab work in the Apparatus at the FH continued today with 2 men from Simmons Concrete. Mike Leon was on site for Dellbrook ,Jim Watt is off this week ,and Mike Leon will be off next week . In the pictures attached you can see the soils in the trench that are not suitable for reusing . The light grey and Tan is Clay and cannot be compacted in the areas of the parking lot .

William Dillon | 12/19/22 | 04:07PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

Attachments



W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/19/22 | 04:08PM

Weather

6:00 AM

34° 

Clear

Wind: 22 MPH | Precipitation: .0" | Humidity: 73%

12:00 PM

38° 

Clear

Wind: 13 MPH | Precipitation: .0" | Humidity: 66%

4:00 PM

40° 

Clear

Wind: 10 MPH | Precipitation: .0" | Humidity: 59%

Work Logs


No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Today there was much activity , 16 Carpenters working at both sites . Shingling started and I had to stop them because they were using staples and the specs called for Nails so they found some nails which met specs and continued . I noticed that the trim called for was 3/4" on windows and corner boards . This should have been 5/4" material ,I believe this was an oversight by K&K . I will do more looking tomorrow morning . There were 4 men working excavating two trenches at both sites ,one to the structure and pole at the TH parking lot. This was over seen by The Concom agent Kara . The trench up through the wetland area under the Boardwalk was started and looked at by Kara . The trench for power and telecom was dug at the EMS out to the pole at Middle road. There were 2 electricians trying to stay ahead of the trench work . The two tight tanks arrived for the EMS building . There were two Roofers working at the EMS building on the back side they have about 80% of the roof done . The two plumbers have moved up to the EMS until the Apparatus bays are poured at the FH , then they can come back and finish all the rough plumbing at the FH . The first phase of slabs will be poured at FH in the apparatus bay tomorrow morning . Mike Leon has called for a Police detail because the trucks may be blocking some of the Crossroad. Mike Leon also said he will be making sure Parking lot lights are working .

William Dillon | 12/20/22 | 05:12PM

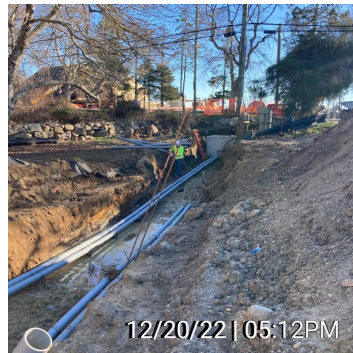



Site Safety Observations No entry

Quality Control Observations No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/20/22 | 05:13PM

Weather

6:00 AM

33° 

Clear

Wind: 9 MPH | Precipitation: .0" | Humidity: 81%

12:00 PM

37° 

Partly Cloudy

Wind: 5 MPH | Precipitation: .0" | Humidity: 78%

4:00 PM

38° 

Clear

Wind: 5 MPH | Precipitation: .0" | Humidity: 75%

Work Logs


No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Team meeting with CHA ,Town members, and Dellbrook team . John Kenny and Antonia arrived late . Tom Seveory went over schedule for the next two weeks . The tank safety people will be out Tomorrow to inspect tank and Silo connections .
The roof on the EMS is almost done with the two Roofers working .
The two Plumbers have been working on both sites .
There were 16 Carpenters working on setting windows ,and exterior insulation at the FH and some working at the EMS finishing up Framing blocking and details .
It was noted that Carpenters nailed Pump Jack supports through the roof shingles ,Mike Leon will address .
There was a discussion regarding the 5/4' vs. 1x trim . I pointed out that it was in the specs as 5/4 and Mike Leon and I both expressed our concern that with the WRB behind the shingles the 1x will not have enough projection. I feel that Mike Leon and Tom from Dellbrook will figure out next steps , Also in the team meeting the parking lot lighting was Finalized.
There was also discussion regarding the over frame to increase roof pitch at the area where it was not correct. John K wanted to use injected high density foam because he wanted no voids , after some talk Mike Leon suggested using no insulation and venting area . I called a building scientist and got his input and he said that Mike Leons suggestion was the best option .
Mike Owen asked about schedule and how the steel fix will effect and Tom S. said no impact on final schedule .
The two slabs were poured at the apprautus bay in the FH , Briggs engineering took samples . There were 5 men from Simmons pouring the slabs , the concrete was pumped and also used to cover primary power duct bank at EMS .
There were 3 men from Farland working on trenching and moving bad trench material to off site .
There were 2 Electricians working on both sites .
Mike Leon has a plan to stormproof the job for the up coming long weekend . I will look it over after noon tomorrow and make sure I am comfortable with preparations

William Dillon | 12/21/22 | 04:54PM

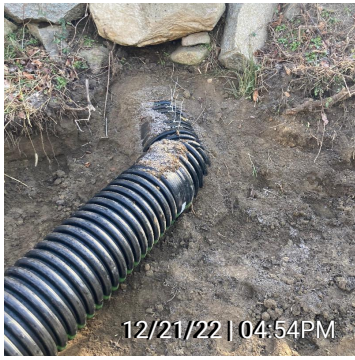

Site Safety Observations No entry

Quality Control Observations No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/21/22 | 04:55PM

Date Thu 12/22/2022

Job #

Prepared By William Dillon



Weather

6:00 AM

38°

Mostly Cloudy

Wind: 8 MPH | Precipitation: .0" | Humidity: 75%

12:00 PM

43°

Mostly Cloudy

Wind: 15 MPH | Precipitation: .0" | Humidity: 81%

4:00 PM

44°

Overcast

Wind: 19 MPH | Precipitation: .0" | Humidity: 85%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Today the Tank safety people were on site and sent one of Farland men into silo to clean out muck and look for leaks .

Mike Leon was on site for Dellbrook, Mike was making sure that everything was buttoned up for the long weekend and coming storm .

The two plumbers were working in the EMS roughing ,they planned to leave by 2:00PM.

The two electricians were working on trench work at both sites

The Roofers have finished the EMS building and have left till the Roof at FH is finalized.

The Carpenters have just about finished porch work at EMS and have been working on the exterior insulation at the EMS. the remaining Carpenters have been shingling at the FH . There were 12 Carpenters onsite . Farland had 2 men working on hauling out fill and inside silo .

Everyone will be gone till next Tuesday and only the Carpenters will be back next week .

Jim Watt will be in for Mike Leon.

Today John Keenan asked Mike Owen to issue a stop work order on all steel revisions until all parties meet and reconcile all plan inconsistencies. I measured the steel angle and agreed with John Keenan regarding slope of steel . I also measured slope of existing 3/12 roof to make sure the new overlay roof actually meets code . What I calculated is the the new 4/12 roof must be 18.57" over the existing 3 3/16" /12" roof not the 14" that Dellbrook has said . I only did this to clear my mind on what was going to be built and actually meet the Zoning ByLaws.

Happy Holidays

Please remember I am always available for questions

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/22/22 | 05:51PM

Date Tue 12/27/2022

Job #

Prepared By William Dillon

Weather

6:00 AM

35° 

Mostly Cloudy

Wind: 20 MPH | Precipitation: .0" | Humidity: 63%

12:00 PM

34° 

Clear

Wind: 15 MPH | Precipitation: .0" | Humidity: 64%

4:00 PM

35° 

Clear

Wind: 14 MPH | Precipitation: .0" | Humidity: 59%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Slow day on site .
Jim Watt for Dellbrook and the Safety Officer were onsite.
There were 6 Carpenters working at both Sites 3 shingling on the FH and 3 working at EMS on exterior siding
William Dillon | 12/27/22 | 05:19PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/27/22 | 05:20PM

Date Wed 12/28/2022

Job #

Prepared By William Dillon

Weather

6:00 AM

34° 

Clear

Wind: 4 MPH | Precipitation: .0" | Humidity: 64%

12:00 PM

41° 

Partly Cloudy

Wind: 16 MPH | Precipitation: .0" | Humidity: 72%

4:00 PM

43° 

Clear

Wind: 19 MPH | Precipitation: .0" | Humidity: 78%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Jim Watt on site for Dellbrook

12 Carpenters working at both sites 4 working on siding at FH and 8 setting windows at EMS , Jim and I discovered some plywood sheathing not nailed at FH so Jim and I will go over both buildings in the AM . We had done this periodically but we must need to do it every day .

There were 4 men from Simmons concrete forming the last of the slabs in the FH apparatus bay ,and they plan to pour next Thursday .

Looks like there will be some people on site tomorrow and none on Friday and Monday for the Holiday.

William Dillon | 12/28/22 | 04:07PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/28/22 | 04:07PM

Weather

6:00 AM

44° 

Mostly Cloudy

Wind: 12 MPH | Precipitation: .0" | Humidity: 85%

12:00 PM

46° 

Partly Cloudy

Wind: 13 MPH | Precipitation: .0" | Humidity: 82%

4:00 PM

46° 

Partly Cloudy

Wind: 14 MPH | Precipitation: .0" | Humidity: 85%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Today Jim Watt was onsite for Dellbrook .
Jim and I reviewed sheathing and window install on both sites.
There were 12 Carpenters working ,4 at the FH on exterior insulation and sheathing ,and 8 at the EMS building on windows and exterior trim .
There were 2 men from Simmons concrete finishing the steel rebar in the apparatus bay at the FH and prepping for Concrete next Wednesday , the pour got moved a day earlier .
Jim said the next two weeks will be very busy with all the trades working in both buildings .
I will be off island tomorrow and Jim will send me a report about what is going on .
Tomorrow Jim will be onsite as well as the Carpenters .
Monday is the Holiday so we will not be seeing any work being done

William Dillon | 12/29/22 | 04:59PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 12/29/22 | 05:00PM

Weather

6:00 AM

44° 

Overcast

Wind: 9 MPH | Precipitation: .0" | Humidity: 97%

12:00 PM

47° 

Possible Light Rain

Wind: 15 MPH | Precipitation: .02" | Humidity: 97%

4:00 PM

49° 

Rain

Wind: 20 MPH | Precipitation: .23" | Humidity: 98%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Jim Watt and Mike Leon were onsite today for Dellbrook .
Today 2 sheetmetal workers were on site installing hangers for ductwork in both buildings pre insulation application.
There were 2 electricians installing conduit it trench between both buildings .
There were 6 carpenters working on siding at FH .
There were 2 men from Farland trenching and getting as built dimensions for site infastructure at the FH with both Jim W. and Mike L.
Mike has arranged to have tank and Silo filled with the Fire Chief but no date set yet as to when.
The 2 plumbers from Delta were working at the EMS .
The Rain in the afternoon sent some men home early

William Dillon | 01/03/23 | 05:22PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 01/03/23 | 05:23PM
