



## Weather

6:00 AM

49° 

Overcast

Wind: 0 MPH | Precipitation: .0" | Humidity: 100%

12:00 PM

73° 

Clear

Wind: 8 MPH | Precipitation: .0" | Humidity: 66%

4:00 PM

59° 

Partially cloudy

Wind: 5 MPH | Precipitation: .0" | Humidity: 100%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Mike Leon and Steve the carpenter in for Dellbrook .  
One side walk has been finished at the TH ,by 2 men from Teles .  
2 carpenters from True Brothers removed the trailer skirting and along with Steve ,and 2 men from Farland Jack it up and pulled it back in preparation to remove trailer on Monday .  
Farland also did prep work for curbing and finished the drainage trench at the bottom of the lower parking area .  
The 2 painters continue in both buildings .  
The other 2 Carpenters were installing doors and hardware in both buildings .  
The 3 Electricians were mostly In the EMS working on IT items .  
Landscaping should be starting by Monday .  
The good news is that the switch gear for the generator has shipped and will be arriving sometime next week .

William Dillon | 06/02/23 | 06:06AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/02/23 | 06:06AM

# Chilmark Fire House and EMS Building

Self

399 Middle Road Chilmark, Massachusetts 02535

Date Fri 06/02/2023

Job #

Prepared By William Dillon



## Weather

6:00 AM

50° 

Overcast

Wind: 3 MPH | Precipitation: .0" | Humidity: 94%

12:00 PM

75° 

Clear

Wind: 10 MPH | Precipitation: .0" | Humidity: 56%

4:00 PM

73° 

Clear

Wind: 10 MPH | Precipitation: .0" | Humidity: 69%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

- Slow day on site as most Fridays are .  
 Steve in for Dellbrook .  
 Steve and 2 carpenters were removing fence screen from the yard side of the job and getting ready for fencing company to come next week to remove all fencing .  
 The 2 painters were still in both buildings and said they will finish everything inside by Wednesday next week ,they will then move outside .  
 1 man from Farland was doing layout for the curbing which will be installed tomorrow .  
 3 electricians working in the EMS .

William Dillon | 06/03/23 | 07:14AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	1 lift William Dillon   06/03/23   07:15AM

## Attachments



W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/03/23 | 07:15AM

# Chilmark Fire House and EMS Building

Self

399 Middle Road Chilmark, Massachusetts 02535

Date Sat 06/03/2023

Job #

Prepared By William Dillon



## Weather

6:00 AM

55°

Overcast

Wind: 17 MPH | Precipitation: .0" | Humidity: 90%

12:00 PM

54°

Overcast

Wind: 29 MPH | Precipitation: .03" | Humidity: 93%

4:00 PM

54°

Overcast

Wind: 31 MPH | Precipitation: .0" | Humidity: 86%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

- Steve Lemare in for Dellbrook .  
3 men in for Farland setting curbs  
2 men working on brick at FH , I mentioned to Steve that the cobbles were not being set to drawing specs and he called Mike Leon to report ,we will look at it again Monday morning .  
William Dillon | 06/04/23 | 07:43AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
-----------	-----	----	-----	-------------

- Any accidents on site today?

2. Any schedule delays occur?

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

1 lift

William Dillon | 06/04/23 | 07:43AM

## Attachments



W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/04/23 | 07:43AM

## Weather

6:00 AM

51° 

Overcast

Wind: 9 MPH | Precipitation: .0" | Humidity: 92%

12:00 PM

57° 

Overcast

Wind: 16 MPH | Precipitation: .0" | Humidity: 77%

4:00 PM

60° 

Partially cloudy

Wind: 16 MPH | Precipitation: .0" | Humidity: 67%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

- Mike Leon and Dan in for Dellbrook .  
 The trailer was emptied and removed from the site in the afternoon.  
 3 Electricians were working on the EMS site .  
 2 painters working on both buildings .  
 The roofer was onsite installing snow guards and working on punch lists items .  
 5 landscapers working on correctly installing the cobbles after my conversation with Mike Leon .  
 The 2 plumbers were working on various tasks in both buildings including tagging valves and installing pipe labels .  
 Farland finished installing the curbing .

William Dillon | 06/06/23 | 05:14AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.


William Dillon | 06/06/23 | 05:15AM



Date Tue 06/06/2023

Job #

Prepared By William Dillon

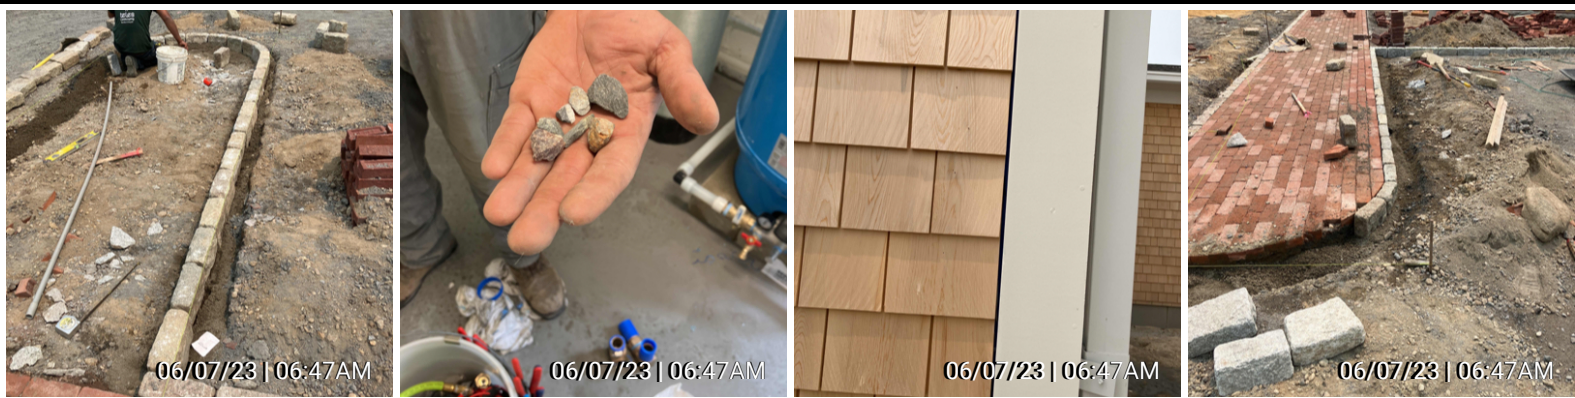

## Weather

6:00 AM	12:00 PM	4:00 PM
<h1>56°</h1> <p><b>Clear</b></p> <p>Wind: 3 MPH   Precipitation: .0"   Humidity: 85%</p>	<h1>69°</h1> <p><b>Clear</b></p> <p>Wind: 9 MPH   Precipitation: .0"   Humidity: 53%</p>	<h1>61°</h1> <p><b>Partially cloudy</b></p> <p>Wind: 13 MPH   Precipitation: .01"   Humidity: 83%</p>

## Work Logs

Name	Description	Quantity	Total Hours
No entry			
Total		0	0

## General Notes

- Mike Leon ,Steve Lemare ,and Dave in for Dellbrook .  
 Mike and I spoke about several things regarding the cobble curbing . Mike had the second in charge at Teles on site and 6 additional men showed up and really got some work done .  
 The 3 Electricians continued in the EMS building .  
 2 men from the security company where installing cameras at the EMS .  
 The Sprinkler company 2 men were finishing items in the Ems Apparatus bays .  
 The 2 plumbers had turned on the water in both Buildings and lost pressure after some problem solving it was determined that the main line from the well to the EMS had stones in it . It was blown clear and was back online by 1:30 ,this was done by Island water systems .  
 Farland had 2 men spreading Loam around the EMS building .  
 Steve and Dave were cleaning up the 2 sites and doing punch list things .  
 The plumber will be getting his final inspection on Wednesday .  
 Ron has been working in all the IT rooms .

Teles had a truck run into the stone wall outside Tim's office . They repaired any damage .  
 William Dillon | 06/07/23 | 06:45AM

## Site Safety Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Landscaping truck hit stone wall William Dillon   06/07/23   06:48AM
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

Attachments



W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/07/23 | 06:48AM

## Weather

6:00 AM

52° 

Clear

Wind: 5 MPH | Precipitation: .0" | Humidity: 89%

12:00 PM

59° 

Partially cloudy

Wind: 11 MPH | Precipitation: .0" | Humidity: 84%

4:00 PM

59° 

Partially cloudy

Wind: 15 MPH | Precipitation: .0" | Humidity: 87%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Today Team Meeting with Dellbrook ,CHA , Chilmark reps. And KAnd K .  
The switch gear Will arrive tomorrow and the Electricans have rented a house so they can stay next week and get everything done ,they will also bring some more bodies to help .They had 3 men working on both sites today .  
The 2 plumbers had final inspections today and all went well .  
Farland's 2 men were spreading topsoil prepping for the gravel pave at the EMS .  
As always the 2 painters were in both buildings .  
The security company was still in the EMS building installing cameras , and equipment . They plan to move down to the FH Thursday.  
The sprinkler company's 2 men were doing final work in the EMS preparing for the test of the system .  
The 6 men from the landscaping company have made good progress at the TH and FH parking it should be ready for gravel pave early next week . They have said some planting material will start arriving by the weekend and planting will start next week .  
There was discussion regarding a guard rail coming into the EMS parking lot and it was decided to install something which will stop vehicles from sliding into Retention pond .

William Dillon | 06/08/23 | 06:21AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

2. Any schedule delays occur?

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/08/23 | 06:22AM

# Chilmark Fire House and EMS Building

Self

399 Middle Road Chilmark, MA 02535




Date Thu 06/08/2023

Job #

Prepared By William Dillon



## Weather

6:00 AM	12:00 PM	4:00 PM
52° 	66° 	66° 
Overcast	Clear	Clear
Wind: 0 MPH   Precipitation: .0"   Humidity: 93%	Wind: 10 MPH   Precipitation: .0"   Humidity: 53%	Wind: 13 MPH   Precipitation: .0"   Humidity: 56%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

- 1. Mike Leon , Dan , and Kyle Gabri in for Dellbrook . Mike left at noon . Dan was cleaning up and Kyle was making lists for Mike Leon. 2 security men were still at the EMS installing equipment . All the switch gear arrived for the generator the 3 Electricians continued at the EMS . 4 landscapers were installing cobbles and brick sidewalks . Farland spread topsoil with 2 men and left at 11:30 It will be a slow day tomorrow , Antonia ,and Jerry from K and K will be on site by 8:am to start a punch list . I will be making my own punch list this morning as well .
- William Dillon | 06/09/23 | 06:24AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/09/23 | 06:25AM

## Weather

6:00 AM

49° 

Partially cloudy

Wind: 0 MPH | Precipitation: .0" | Humidity: 100%

12:00 PM

63° 

Rain, Overcast

Wind: 4 MPH | Precipitation: .0" | Humidity: 71%

4:00 PM

66° 

Clear

Wind: 9 MPH | Precipitation: .0" | Humidity: 66%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Mike Leon and Dan Carll in for Dellbrook .  
The 3 electricians were setting the switch gear at the generator .  
The 2 painters were still in the EMS .  
Dellbrook had 2 men cleaning up inside both buildings to prep for the cleaners.  
The 2 men working on security were still in the EMS and were not expecting to finish today .  
I met with Antonia and Jerry from K And K, we walked both buildings for 2 hours and did a punch list . I left them after we went through both buildings and they were going to photograph all the items .  
The landscapers had 3 men when I was there .

William Dillon | 06/10/23 | 07:24AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/10/23 | 07:25AM



## Weather

6:00 AM

51° 

Overcast

Wind: 0 MPH | Precipitation: .0" | Humidity: 96%

12:00 PM

69° 

Partially cloudy

Wind: 5 MPH | Precipitation: .0" | Humidity: 56%

4:00 PM

64° 

Rain, Partially cloudy

Wind: 5 MPH | Precipitation: .0" | Humidity: 69%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

- Just went by to check on landscapers today . I did not see any onsite . There were 4 cleaning people working in the EMS building and they had finished the office area of the FH .  
William Dillon | 06/11/23 | 07:02AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?				

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/11/23 | 07:03AM

## Weather

6:00 AM

61° 

Clear

Wind: 3 MPH | Precipitation: .0" | Humidity: 97%

12:00 PM

71° 

Clear

Wind: 13 MPH | Precipitation: .0" | Humidity: 82%

4:00 PM

72° 

Partially cloudy

Wind: 10 MPH | Precipitation: .0" | Humidity: 77%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Mike Leon and Dan Carll in for Dellbrook.  
Farland started to install the paving mats but I spoke to Mike Leon and stopped them because the specs said that metal edging should be installed before paving mats are installed .  
The furniture was installed and I watch over installation.  
The 4 electricians were working in both buildings .  
Ron was working on IT in both buildings .  
Teles did not show up to work at all .Mike said he and Tom have been really working on them to get working . Mike continues to stay upbeat regarding the finish date

William Dillon | 06/13/23 | 12:39PM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/13/23 | 12:40PM

## Weather

6:00 AM

62° 

Rain, Overcast

Wind: 1 MPH | Precipitation: .01" | Humidity: 97%

12:00 PM

71° 

Overcast

Wind: 9 MPH | Precipitation: .0" | Humidity: 87%

4:00 PM

69° 

Partially cloudy

Wind: 12 MPH | Precipitation: .0" | Humidity: 79%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Mike Leon and Dan carll in for Dellbrook .  
4 electricians working in both buildings .  
Farland had 3 men working on some punch list items and spreading top soil .  
There were 3 men installing alarm and security equipment in both buildings .  
The garage door men were installing weather stripping and adjusting the door hardware.  
Ron was installing TV monitors in several places in the EMS .  
The 2 plumbers were on site briefly to do some punch list items ,the last few items on their list should be done this week .  
The 2 painters are still painting and doing items of the punch list and their list at EMS in nearly complete.  
I did not see any action from the landscapers before 1 when I left .  
The 3 iron workers were onsite to install the Boardwalk Railing but it had not been delivered by 1 when I left for the day .

William Dillon | 06/14/23 | 05:56AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?


6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/14/23 | 05:57AM

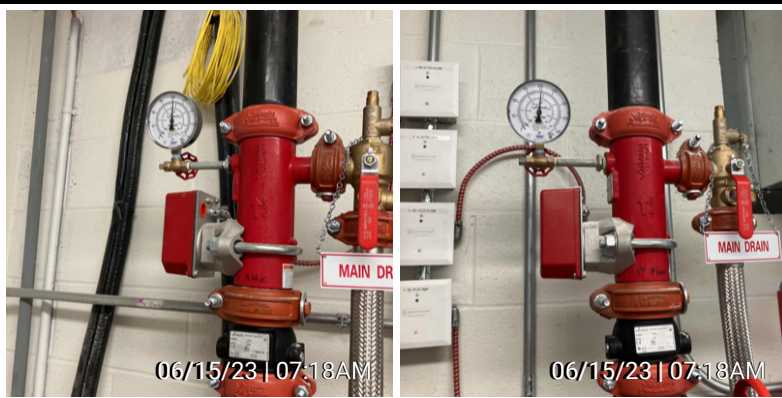

## Weather

6:00 AM

61°

Partially cloudy

Wind: 9 MPH | Precipitation: .0" | Humidity: 93%

12:00 PM

63°

Partially cloudy

Wind: 11 MPH | Precipitation: .0" | Humidity: 90%

4:00 PM

64°

Rain, Partially cloudy

Wind: 15 MPH | Precipitation: .01" | Humidity: 93%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Team meeting with Dellbrook , K and K , and committee .  
 Tom and Mike say things still on track for the 28th.  
 Plants coming tomorrow ,and landscape Architect is coming over in the morning .  
 I went and saw Reid Silva twice yesterday to make sure he was going to attend the Con Com Meeting and to get some details for paving and rain garden retention pond .  
 5 landscapers were working on the paving mat at the EMS .  
 3 iron workers were working on the railings at stairs and at the Boardwalk .  
 4 electricians were working in both buildings .  
 There was 1 man from Simmons grinding concrete in the FH . This was part of the punch list .  
 The 2 sprinkler men were testing the system and it held 200 lbs of pressure for 2 hours .  
 The 2 painters continue in both buildings .  
 Dan Carll from Dellbrook was getting all the keys sorted out in preparation for hand off.

William Dillon | 06/15/23 | 07:17AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/15/23 | 07:18AM



## Weather

6:00 AM

61° 

Clear

Wind: 8 MPH | Precipitation: .0" | Humidity: 85%

12:00 PM

70° 

Partially cloudy

Wind: 12 MPH | Precipitation: .0" | Humidity: 66%

4:00 PM

72° 

Clear

Wind: 14 MPH | Precipitation: .0" | Humidity: 60%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Mike Leon and Dan Carll onsite for Dellbrook .  
The landscape architect arrived around 9:15 he was wanting to meet landscape crew to go over planting .  
The Teles crew did arrive by 9:30 and did start moving plants .  
The 5 people from Farland were installing the paving and Jack hammering out the curbs to reinstall .  
The 3 iron workers were installing the Boardwalk railings . Mike Leon had 2 Carpenters helping with build out blocks for railing install .  
The 2 painters are the ever ready bunnies of the job they never stop .  
The 4 electricians were in both buildings all day .  
There was 1 man setting up the kitchen hoods in both buildings .  
Ron was also in both buildings setting up IT , phones and Monitors .  
I will be off island tomorrow for continuing Ed so I will not send a report till mid day Saturday .  
The buildings will be locked going forward Ron and I will have the access information  
If people want to see the buildings . I am mostly available at any time , if you would like to do a walk through please let me know and I will give you a walk through .

William Dillon | 06/15/23 | 06:13PM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/15/23 | 06:14PM

## Weather

6:00 AM

54° 

Partially cloudy

Wind: 0 MPH | Precipitation: .0" | Humidity: 97%

12:00 PM

70° 

Clear

Wind: 8 MPH | Precipitation: .0" | Humidity: 62%

4:00 PM

69° 

Clear

Wind: 10 MPH | Precipitation: .0" | Humidity: 68%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Mike Leon ,Dan Carll , and Steve Lemare in for Dellbrook .  
I picked up the plans from Reid Silva regarding the drainage pond at the end of the EMS parking lot and gave it to Mike Leon .  
The 2 plumbers were hooking up the last few things and removing all their gear and tools they will be back to install EMS Decon sink .  
The 5 carpenters were doing punch list items on both buildings .  
The 4 Electricans continued in both buildings .  
Farland had 4 people spreading the gravel in the EMS parking area .  
There were 8 landscapers both planting and working on the brick at the TH .  
At. The end of the day the fence company arrived and started taking down the temporary Fencing .  
William Dillon | 06/20/23 | 06:17AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/20/23 | 06:17AM

## Weather

6:00 AM

58° 

Partially cloudy

Wind: 10 MPH | Precipitation: .0" | Humidity: 93%

12:00 PM

59° 

Partially cloudy

Wind: 11 MPH | Precipitation: .0" | Humidity: 93%

4:00 PM

59° 

Partially cloudy

Wind: 11 MPH | Precipitation: .0" | Humidity: 93%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Mike L, Dan C. And Steve L. In for Dellbrook .  
Paving was finished at EMS and FH this was done with 5 men from Daniels Paving .  
Line striping will be done tomorrow .  
We will not be able to use parking area until next Monday .  
American Electric had 4 men working on both buildings , they also had the generator tech start up the Generator everything worked as it was supposed to .  
Apex also had 2 Electricans doing control wiring at generator and in both buildings .  
Farland had 4 workers installing the gravel pave at the FH .  
Teles has finished the brick walls at the FH with 4 men .

William Dillon | 06/21/23 | 06:34AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

Paving is off limits until next week  
William Dillon | 06/21/23 | 06:35AM

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/21/23 | 06:35AM

## Weather

6:00 AM

53° 

Clear

Wind: 5 MPH | Precipitation: .0" | Humidity: 90%

12:00 PM

67° 

Clear

Wind: 16 MPH | Precipitation: .0" | Humidity: 64%

4:00 PM

67° 

Clear

Wind: 18 MPH | Precipitation: .0" | Humidity: 62%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Team meeting day with Chilmark Committee , Dellbrook Team, and K and K.  
The decision was made to delay the Ribbon cutting until July 12 th . This way the load test , life safety and occupancy permit are all completed.  
Farland was working in the TH parking lot area working on the Gravel paving with 5 people ,they will be demobilizing all their equipment Thursday at 11. They plan to come back after Landscapers on done with the bulk of the landscaping to do some odds and ends that have .  
The 3 Electricians were working once again on both sites .  
Dan Carll and Steve Lemare from Dellbrook were working on punch list items in both buildings .  
2 carpenters from True Brothers were helping with Gravel Pave and started the TH deck repair the Teles crew were moving plants in preparation for planting .  
The Town Hall parking lot will open in some form on this coming Monday ,Mike Leon will let us all know in what form that will be.

William Dillon | 06/22/23 | 06:06AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

Areas that are only accessible across the paving will not be able to be worked on in order to let Paving set .

William Dillon | 06/22/23 | 06:08AM

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/22/23 | 06:08AM



## Weather

6:00 AM

60° 

Overcast

Wind: 9 MPH | Precipitation: .0" | Humidity: 79%

12:00 PM

66° 

Overcast

Wind: 19 MPH | Precipitation: .0" | Humidity: 71%

4:00 PM

62° 

Overcast

Wind: 16 MPH | Precipitation: .0" | Humidity: 92%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Mike Leon ,Steve Lemare and Dan Carll in for Dellbrook .  
Steve and Dan were working on punch list items in both buildings and setting Handicap signs at EMS .  
There were 6 Electricians working in both buildings , 3 from American Electric and 3 from Apex working on control integration .  
The 2 painters continue working on Punch items .  
Farland worked with 5 people on the TH parking area , they were helped out by 2 carpenters from True Brothers.  
Teles had 4 men setting plants , Bill Rossi will be going on site to view and over see planting placement on Friday morning .

William Dillon | 06/23/23 | 05:45AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

Some areas where new paving was installed.

William Dillon | 06/23/23 | 05:46AM

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/23/23 | 05:46AM

## Weather

6:00 AM

62° 

Overcast

Wind: 4 MPH | Precipitation: .0" | Humidity: 97%

12:00 PM

70° 

Overcast

Wind: 8 MPH | Precipitation: .0" | Humidity: 87%

4:00 PM

72° 

Clear

Wind: 9 MPH | Precipitation: .0" | Humidity: 79%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Mike Leon ,Dan Carll ,and Steve Lemare in for Dellbrook .  
Lots of Landscaping going on Bill Rossi was at the EMS building talking to Peter Rebello who is the foreman for Teles . Peter was confidant that they will get everything into the ground and watered . Bill Rossi said he felt good knowing that Peter was overseeing the install.  
There were 2 Electricians over seeing the 2 control wiring Electricians from Apex .  
Ron was working on IT stuff with his son .

William Dillon | 06/25/23 | 06:50AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/25/23 | 06:51AM

Date Mon 06/26/2023

Job #

## Weather

6:00 AM

68° 

Overcast

Wind: 4 MPH | Precipitation: .0" | Humidity: 100%

12:00 PM

75° 

Partially cloudy

Wind: 10 MPH | Precipitation: .0" | Humidity: 89%

4:00 PM

74° 

Overcast

Wind: 13 MPH | Precipitation: .0" | Humidity: 90%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Mike Leon and Dan Carll in for Dellbrook.  
Things winding down on the job .  
2 Electricians 1 working on paperwork documentation and another doing punch list things .  
I have still been trying to get Well Contractor to the site to start up filters, he has told me he will be onsite Wednesday .  
Farland had 3 men working in the parking lot at the FH and that is 99% done .  
Teles had 3 men planting at the EMS .  
The 1 carpenter was working repairing deck and ramp at the TH .

William Dillon | 06/27/23 | 07:44AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

## Weather

6:00 AM

70° 

Rain, Overcast

Wind: 5 MPH | Precipitation: .03" | Humidity: 94%

12:00 PM

68° 

Partially cloudy

Wind: 17 MPH | Precipitation: .02" | Humidity: 97%

4:00 PM

67° 

Partially cloudy

Wind: 16 MPH | Precipitation: .0" | Humidity: 100%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

- Ike Leon and Dan Carll and Kyle Gabri onsite for Dellbrook .  
There was a washout at the EMS parking area . I called Reid Silva right away and he came out to witness the flowing water and determine how to avoid future water problems . We were lucky in some ways that this happened before Dellbrook has finished . We will discuss in tomorrows meeting.  
The garage door sub came to fix the one broken door at the EMS .  
THE 2 Electricians were doing punch list items .  
Ron had 2 men helping him on IT stuff.there was 1 carpenter doing punch list items .  
There were several landscapers working in the AM but left as the rain continued .  
William Dillon | 06/27/23 | 04:10PM
- I also met with Cole Powers and he will be wiring the siren in the next few days  
William Dillon | 06/27/23 | 04:11PM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/27/23 | 04:11PM



## Weather

6:00 AM

70° 

Rain, Overcast

Wind: 14 MPH | Precipitation: .09" | Humidity: 94%

12:00 PM

73° 

Partially cloudy

Wind: 16 MPH | Precipitation: .0" | Humidity: 88%

4:00 PM

67° 

Partially cloudy

Wind: 13 MPH | Precipitation: .0" | Humidity: 100%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Team meeting and committee meeting today .  
there were no Landscapers on site today .  
The 2 painters are still doing patching .  
The security men were doing final wiring of cameras at FH .  
The Farland crew was spreading dense mix and setting curb stops .  
It was decided to move wardrobes in Bunk-rooms to make TVs work in the 2 rooms.  
I spoke to Reid Silva regarding the washout and he said he would send his repair plan and drainage fix out today .  
Things are winding down on the job .  
Joe Tierny was onsite doing some inspections ,the alarm inspection went well and passed .

William Dillon | 06/28/23 | 04:08PM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/28/23 | 04:10PM

## Weather

6:00 AM

66° 

Partially cloudy

Wind: 5 MPH | Precipitation: .0" | Humidity: 95%

12:00 PM

71° 

Overcast

Wind: 8 MPH | Precipitation: .0" | Humidity: 86%

4:00 PM

73° 

Clear

Wind: 10 MPH | Precipitation: .0" | Humidity: 83%

## Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

## General Notes

1. Mike Leon ,Dan Carll, and Steve Lemare in for Dellbrook.  
1 Carpenter and Dan Carll worked on Board walk stairs .  
The welders were working reversing the railing angles .  
The 2 painters were working on both buildings .  
Farland had 3 men setting parking stops and drip trench stone .

William Dillon | 06/30/23 | 09:13AM

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

6. Any equipment rented on site?

W D

---

I, William Dillon, have reviewed and completed this report.

William Dillon | 06/30/23 | 09:13AM
