

Date Fri 03/03/2023

Job #

Prepared By William Dillon

Weather

6:00 AM

35° 

Clear

Wind: 6 MPH | Precipitation: .0" | Humidity: 64%

12:00 PM

46° 

Clear

Wind: 4 MPH | Precipitation: .0" | Humidity: 39%

4:00 PM

42° 

Clear

Wind: 7 MPH | Precipitation: .0" | Humidity: 50%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Today onsite Mike Leon from Dellbrook was overseeing the fine tuning of the ram jacks final installation . The well company had installed two well tanks in the EMS instead of 1 tank in each building as was planed . I called the well company and they came right out and move 1 tank to the FH . There were 5 sheet rockers working in the FH 4 hanging in the Apparatus bays and 1 taping in the electric rooms . I noticed that the Hat channel on the bottom of the Trusses in the Apparatus bay was installed on 16" centers not 24" centers as was on the plan . Mike Leon said that he felt 24" would not be sufficient and that the drywall would sag . So Mike had the rockers install the channel closer together. That was a good call by Mike . There was 1 man hanging ductwork in the EMS . Joe Tierney came and did an inspection at the EMS . We are still waiting for some more info from Reid Silva .

William Dillon | 03/04/23 | 08:24AM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/04/23 | 08:24AM

Chilmark Fire House and EMS Building


Self

399 Middle Road Chilmark, Massachusetts 02535

Date Mon 03/06/2023

Job #

Prepared By William Dillon

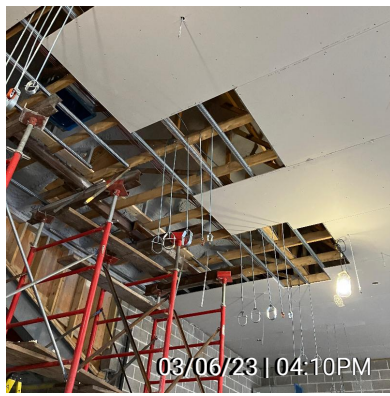

Weather

6:00 AM

39° 

Clear

Wind: 12 MPH | Precipitation: .0" | Humidity: 63%

12:00 PM

50° 

Clear

Wind: 12 MPH | Precipitation: .0" | Humidity: 34%

4:00 PM

42° 

Partially cloudy

Wind: 20 MPH | Precipitation: .0" | Humidity: 60%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Mike Leon on site for Dellbrook .

There were 4 sheet-rockers working at the FH framing metal ceilings in the Decon room and storage rooms and Hallways .

The Painter arrived around noon to prime walls in FH .

In the Decon room I noticed that there should be more sprayed insulation behind shower and in exterior wall . I asked Mike Leon to get it done next time the insulators come .

Simmons concrete was there setting forms for concrete stairs at the top and bottom of parking area at EMS. I noticed that in the Drawings it showed 5 risers and it actually required 7 risers to make it work . Mike Leon said he asked John K about it and John just said make it work .

There were 4 electricians pulling wires to the Generator panel at the EMS .

The 2 plumbers were back and they were working on the tight tank plumbing at the EMS which is what was holding up the concrete apron .

I expected to see the steel workers at the job this morning and Mike said that they will be coming on Wednesday , Mike spoke to the FC regarding someone onsite while the welding was happening .

The well contractor had not shown up as of noon to move 1 of the tanks .

Farland was working on the drainage system behind the EMS building with 2 men , Farland was able to get washed stone so that wont be a holdup.

William Dillon | 03/06/23 | 04:09PM

Site Safety Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	2 lifts William Dillon 03/06/23 04:12PM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/06/23 | 04:12PM

Weather

6:00 AM

36° 

Clear

Wind: 9 MPH | Precipitation: .0" | Humidity: 38%

12:00 PM

42° 

Clear

Wind: 10 MPH | Precipitation: .0" | Humidity: 35%

4:00 PM

42° 

Overcast

Wind: 14 MPH | Precipitation: .0" | Humidity: 40%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Today I met Mike Owen on site and we spent 2 hours going over the Change order Log in preparation for meeting this Friday.
Mike Leon was onsite for Dellbrook .
There were 2 men from Simmons working on setting forms for lower stairs at EMS parking lot.
The 4 electricians were still pulling service wires at both locations .
The 2 Plumbers were installing the gas line into the EMS .
The 4 sheet-rockers were installing Door frames at the EMS
There were 2 men doing sheetrock taping , and 1 man painting in the FH .
Farland had 2 men installing the Culteck drainage and recharge system at the EMS .
I saw Cody Coutino From VLS at the EMS checking on the Culteck system , Cody, Mike Leon , and I discussed what was needed for the ADA ramps and how Cody could help get things done so nothing holds up job .
I spent another hour looking at various aspects of the job with Mike Owen . We both feel that the job is going pretty well . We both have the feeling from Dellbrook that they are trying to do a good job
William Dillon | 03/07/23 | 05:37PM
2. Mike Leon also said Steel work will start Wednesday morning at FH .
Mike also said Garage doors will be started on the 14 of March
William Dillon | 03/07/23 | 05:38PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions N/A No Yes Description

1. Any accidents on site today?

2. Any schedule delays occur?

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/07/23 | 05:38PM

Weather

6:00 AM

32° 

Partially cloudy

Wind: 19 MPH | Precipitation: .0" | Humidity: 64%

12:00 PM

45° 

Overcast

Wind: 23 MPH | Precipitation: .0" | Humidity: 54%

4:00 PM

47° 

Overcast

Wind: 21 MPH | Precipitation: .0" | Humidity: 50%

Work Logs




No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Team meeting was remote today. Mike Owen and Aditya could not make it .
The schedule was covered and things are still looking good .
Mike Leon got Jim Watt back to help him run the job .
The 4 Electricians continued pulling secondary wires into buildings in preparation for Eversource to install the Transformers .
3 men from Simmons concrete poured the top stair at the EMS parking lot .
The 2 Carpenters were removing the cheek wall above the steel in the FH .
The 3 steel workers were welding the steel plate on the bottom of the beam at the FH
The 1 Painter has ben painting walls in both buildings ,including some of the block walls .
There were several hundred sheets of drywall delivered to the EMS and hanging has started with 4 sheet-rockers .
Mike Leon stated the unsuitable soil problem at the FH in the area of the 2 tight tanks in the front of the FH , we all agreed that it would be done as T and M . This just has to happen and there is no way around it .
The Town will be getting a credit for the gas line changes at the FH .
I will need to keep staying in touch with Reid Silva in order to keep Dellbrook working on finished grades .
Farland has finished the Cultec drainage at the EMS and started working on Misc. projects on site they had 2 men

William Dillon | 03/08/23 | 06:54PM

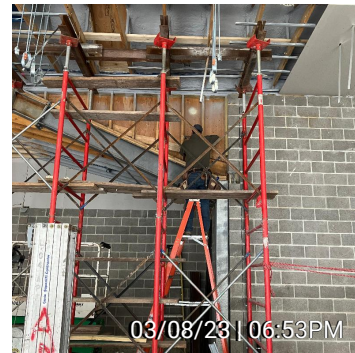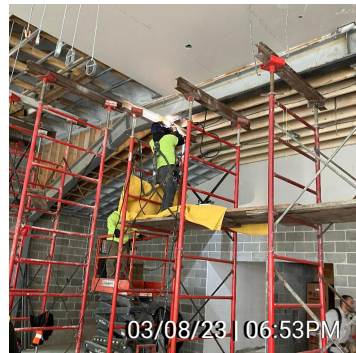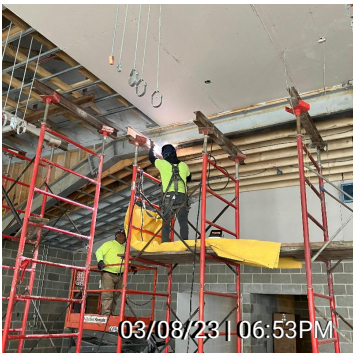

2. There will be a Change Order meeting on Friday at 11:30 with CHA, myself ,K and K and Dellbrook . this will finalize the COR to date we hope

William Dillon | 03/08/23 | 06:59PM

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	3lifts and 1 geni lift William Dillon 03/08/23 06:56PM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/08/23 | 06:56PM

Weather

6:00 AM

38° 

Overcast

Wind: 10 MPH | Precipitation: .0" | Humidity: 65%

12:00 PM

48° 

Clear

Wind: 14 MPH | Precipitation: .0" | Humidity: 40%

4:00 PM

46° 

Clear

Wind: 18 MPH | Precipitation: .0" | Humidity: 54%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Today Mike Leon and Jim Watt were on site for Dellbrook .
I was at site around 7:45 am to see the progress on the steel fix from the steel workers, there were 3 of them . The steel beams that were made for the fix did come with the correct angle where they mate with the upper steel beam. Mike Leon was in the process of calling and finding out how to proceed from the structural designer . This will not slow progress or schedule but still a small problem . I notified Michael Owen right away .
The bottom stairs were formed and will be poured tomorrow morning , 2 men from Simmons working on that.
The Electricians were working on both buildings and there were 4 of them .
The 2 plumbers were working on both buildings .
There were 2 Carpenters working on removing the walls over the steel in the FH .
4 sheet-rockers were hanging rock in the EMS.
Farland had 2 men working on various tasks at the EMS site .
The 2 big bosses from Dellbrook visited site today as did Dan Dellbrook's Safety officer.
In the picture you can see how the steel did not mate properly.

William Dillon | 03/09/23 | 05:08PM



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	3 lifts William Dillon 03/09/23 05:08PM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/09/23 | 05:08PM

Date Fri 03/10/2023

Job #

Prepared By William Dillon

Weather

6:00 AM

28° 

Clear

Wind: 3 MPH | Precipitation: .0" | Humidity: 95%

12:00 PM

45° 

Clear

Wind: 14 MPH | Precipitation: .0" | Humidity: 53%

4:00 PM

45° 

Clear

Wind: 15 MPH | Precipitation: .0" | Humidity: 63%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- Slow day at site today.
Only 1 painter and Jim Watt for Dellbrook .
All the other Trades worked 4 10 hour Days .
The incorrect steel has been removed and As of last night there was a new plan .
Mike Owen ,myself , Tom Shevory, aditya, and John Keenan met for 2 hours going over change orders. The Chief was at FH in the AM as Fire watch for any welding .
The welder and steel worker went to a different site .

William Dillon | 03/11/23 | 07:01AM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/11/23 | 07:02AM

Weather

6:00 AM

32° 

Clear

Wind: 4 MPH | Precipitation: .0" | Humidity: 92%

12:00 PM

44° 

Overcast

Wind: 14 MPH | Precipitation: .0" | Humidity: 76%

4:00 PM

43° 

Overcast

Wind: 12 MPH | Precipitation: .0" | Humidity: 88%

Work Logs



No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Today on site Mike Leon and Jim Watt .
Mike explained that this week he was loosing the Excavation contractor due to the weather.
The 3 Electricians on site today and the 2 Plumbers will be the only ones on the site tomorrow if the boats dont run .
I met with the well contractor to go over the scope of his work , I will review that scope with the Plumber in the AM
The 1 Painter has been painting the CMU walls in both buildings .
There were 6 Sheetrockers working in the EMS and 2 working in the FH
The Overhead doors arrived on Saturday and are onsite .

William Dillon | 03/13/23 | 04:47PM

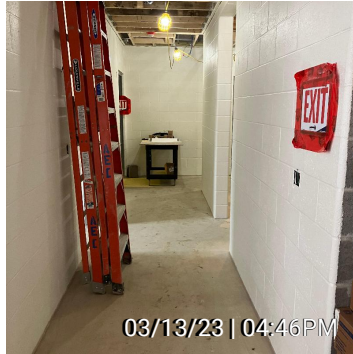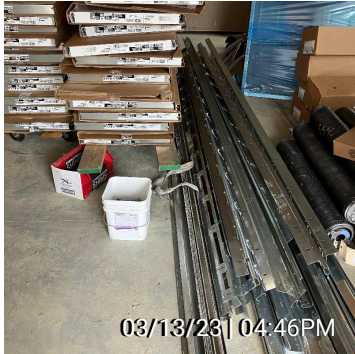

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	lost week on outside William Dillon 03/13/23 04:49PM
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	2 lifts William Dillon 03/13/23 04:49PM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/13/23 | 04:49PM

Weather

6:00 AM

45° 

Rain, Overcast

Wind: 17 MPH | Precipitation: .03" | Humidity: 90%

12:00 PM

41° 

Overcast

Wind: 21 MPH | Precipitation: .0" | Humidity: 93%

4:00 PM

40° 

Rain, Overcast

Wind: 17 MPH | Precipitation: .0" | Humidity: 87%

Work Logs


No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- No Dellbrook people on site today .
2 plumbers working on FH
The Garage door installers were working on installing doors at FH .
There were 3 Electricians working on the FH and EMS .
The commercial entry door was installed at the FH and by 2 men.
I expect Dellbrook back in the Am

William Dillon | 03/14/23 | 06:16PM

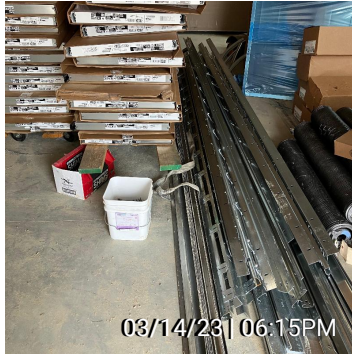

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
-----------	-----	----	-----	-------------

1. Any accidents on site today?

2. Any schedule delays occur?

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

2 lifts

William Dillon | 03/14/23 | 06:16PM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/14/23 | 06:16PM

Weather

6:00 AM

38° 

Overcast

Wind: 18 MPH | Precipitation: .0" | Humidity: 73%

12:00 PM

44° 

Partially cloudy

Wind: 18 MPH | Precipitation: .0" | Humidity: 51%

4:00 PM

45° 

Overcast

Wind: 17 MPH | Precipitation: .0" | Humidity: 44%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Things back to normal today after the non storm .

We did still lose the excavators for the week but in the weekly meeting today Tom Shevory said things are still tracking for the same finish dates.

The 2 plumbers were working on both sites .

There were 3 electricians working in the FH .

The Painter was painting CMU walls .

The garage door contractor was installing the last door at the EMS , there was quite a bit of discussion before during and after the meeting regarding the motor position and a resolution was reached and all parties were happy . The motors delivered will be returned and new side mount motors will be installed with helper springs.

The glass company was installing the entry door at the EMS and will continue on the EMS till they are done . Mike Leon will figure out a way to protect them from Damage .

The 3 sheet rockers were working setting door jambs and sheet-rocking in the EMS.

There was 1 sheet-rocker taping ceiling in the apprautus bay at the FH .



We discussed the drainage at the FH in the meeting and we hope to have a resolution by next week as Farland gets final structures set at both sites .

Mike Owen ,Bill Rossi ,and I will meet tomorrow at 11 to go over the COR logs .

Mike Leon says that there still no reportable accidents to date on site .

Next week Tuesday and Wednesday Dellbrook will shut down the TH parking lot to install septic tank and hook up for septic for the FH and install the tank at the EMS.

William Dillon | 03/15/23 | 06:00PM

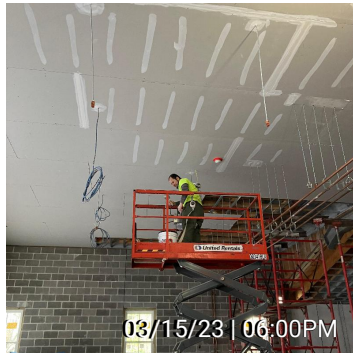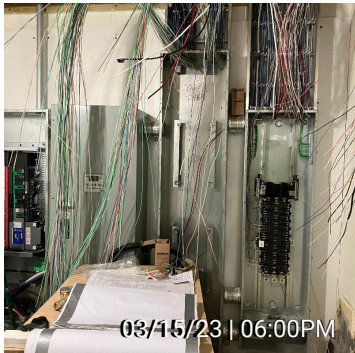

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	2 lifts William Dillon 03/15/23 06:01PM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/15/23 | 06:01PM

Weather

6:00 AM

36° 

Clear

Wind: 16 MPH | Precipitation: .0" | Humidity: 53%

12:00 PM

48° 

Clear

Wind: 15 MPH | Precipitation: .0" | Humidity: 23%

4:00 PM

43° 

Partially cloudy

Wind: 17 MPH | Precipitation: .0" | Humidity: 64%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Mike Leon and Jim Watt on site for Dellbrook .
The 2overhead Door men were hoping to get 3 of the doors installed at the FH.
The 2 men installing the aluminum door jambs and doors have finished installing all 4 doors at both sites , they were now starting to install the closing hardware ,Mike was going to figure out a way to protect them .
Sheet rock is about 80% done with the hanging at the EMS building .
Also at the EMS I walked the cat walk and look at the work being done by the 2 Tin Knockers every joint had been coated with duct seal as is in the specs .
The 2 electricians were working at the FH in the IT room .
1 sheet rocker was in the FH continuing to tape walls and ceilings .
The lone painter continued in both buildings painting the CMU walls .
I was able to speak to Reid Silva and get him working on RFI 65 which we need to finish the sidewalks and parking areas on both sites .

William Dillon | 03/17/23 | 07:43AM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

2 lifts

William Dillon | 03/17/23 | 07:44AM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/17/23 | 07:44AM

Weather

6:00 AM

30° 

Clear

Wind: 0 MPH | Precipitation: .0" | Humidity: 88%

12:00 PM

48° 

Overcast

Wind: 21 MPH | Precipitation: .0" | Humidity: 61%

4:00 PM

51° 

Clear

Wind: 17 MPH | Precipitation: .0" | Humidity: 74%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. This morning I saw Mike Leon and Jim Watt remeasuring for steel replacement they needed to get quite a few new measurements for the steel,fab company .
There was 1 tin Knocker at the EMS .
6 sheet rockers 4 at EMS and 2 working at FH .
The metal door guys had finished by 10 and will be back for latches in the future .
The 2 overhead guys had finished 3 doors at the FH and gone home by 2:30.
There will be a Sheetrock delivery on Saturday which will be the build of the order to finish the EMS .
John Keenan asked me to ask Mike Leon to protect the new doors I,forwarded his email to me to Mike .

William Dillon | 03/17/23 | 05:34PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

2 lifts

William Dillon | 03/17/23 | 05:34PM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/17/23 | 05:34PM

Weather

6:00 AM

32° 

Clear

Wind: 6 MPH | Precipitation: .0" | Humidity: 48%

12:00 PM

44° 

Clear

Wind: 19 MPH | Precipitation: .0" | Humidity: 39%

4:00 PM

44° 

Clear

Wind: 16 MPH | Precipitation: .0" | Humidity: 41%

Work Logs


No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Today Mike Leon on site for Dellbrook .
The site work started back up after losing last week . Farland had 3 men digging for Septic tank at FH . TH parking lot will be closed for 2 days starting tomorrow while tank is set and septic line is installed . The Siren pole will be moved and set this week and then septic line can be installed . Mike Leon says we will have TH parking back later in the week .
There were 3 Electricians working at the FH .
The 1 Painter had started putting color on walls at FH .
2 men were working in the FH working on the over head doors.
There were 4 sheet rockers starting in the apparatus bay in the FH by 11:00 am

William Dillon | 03/20/23 | 06:22PM

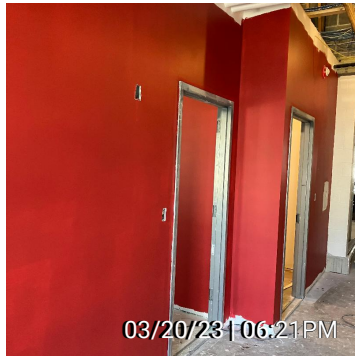

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	2 Lifts William Dillon 03/20/23 06:23PM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/20/23 | 06:23PM

Weather

6:00 AM

35° 

Clear

Wind: 3 MPH | Precipitation: .0" | Humidity: 85%

12:00 PM

54° 

Clear

Wind: 13 MPH | Precipitation: .0" | Humidity: 42%

4:00 PM

52° 

Clear

Wind: 15 MPH | Precipitation: .0" | Humidity: 37%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- Today, I was onsite at 7:30 because the septic tank and pump chamber were to be excavated and set at the FH. as soon as digging started we could see problems, the hole kept caving in and collapsing. The tanks arrived later than they thought they would. The excavator and Mike Leon were worried, I called Reid and asked for some guidance. Reid said to dig as best we could, Dewater and set tanks. He was planning on sending Cody to look at soil conditions. at around 1 PM it was decided to not have Goodale set tank because of the worry regarding more collapsing of excavation. Tomorrow morning Baxter crane company will be on site to set both tanks, then Farland can back fill and finish FH site. The Fire Department has been standing by to fill tanks so they wont float. Tomorrow the siren pole will be set and eversource will be setting the transformers at both sites. There were 3 electricians working on both sites. There was 4 sheet rockers working at both sites 3 working on metal ceilings at the EMS. There was 1 pipe insulator working at the EMS. The overhead door question regarding the openers has been resolved and the new motors will be on site in the AM.

William Dillon | 03/21/23 | 06:38PM



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	2 lifts William Dillon 03/21/23 06:38PM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/21/23 | 06:38PM

Weather

6:00 AM

31° 

Clear

Wind: 3 MPH | Precipitation: .0" | Humidity: 93%

12:00 PM

53° 

Clear

Wind: 1 MPH | Precipitation: .0" | Humidity: 44%

4:00 PM

44° 

Partially cloudy

Wind: 10 MPH | Precipitation: .0" | Humidity: 82%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- Today the 2 tanks were set at the FH by Farland and Baxter Crane .
The 2 men continued working on overhead doors at the FH .
Team meeting at 10 covered the 10 week look ahead schedule to completion which we will get from Dellbrook every week now .
A milestone today was having Chief Bradshaw arrange for Eversource to move and install the Siren at the EMS .
The 1 painter continued putting color on the walls at the FH .
The 3 electricians were working on both sites wiring into the service panels .
The 4 sheet rockers were hanging metal framing for ceilings in the EMS, and 2 were working on taping the ceiling at the FH.
2 men from Simmons were forming up, sidewalks behind the EMS .
There were 2 men from Yankee Sprinkler installing heads in the EMS .
The 2 plumbers were back on site at midday .
There was 1 man doing pipe insulation in the EMS.
Lots of different subs on site ,once the Sheetrock is done and cleaned up the entire site will change as finishes get started

William Dillon | 03/23/23 | 07:23AM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions N/A No Yes Description

1. Any accidents on site today?

2. Any schedule delays occur?

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

2 lifts

William Dillon | 03/23/23 | 07:23AM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/23/23 | 07:23AM

Weather

6:00 AM

48° 

Overcast

Wind: 6 MPH | Precipitation: .0" | Humidity: 97%

12:00 PM

51° 

Partially cloudy

Wind: 15 MPH | Precipitation: .0" | Humidity: 83%

4:00 PM

47° 

Rain, Overcast

Wind: 10 MPH | Precipitation: .03" | Humidity: 93%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Today Mike Leon and Jim Watt in for Dellbrook
Farland had 3 men backfilling and compacting the fill around septic tank and pump chamber at FH .
The 2 men from the overhead door company we're installing the lift Motors ,
One of the doors at the FH will need some work as the floor the slab was poured 1" to low .
Simmons has ordered an epoxy grout and pre treatment to raise the floor level .
The 3 electricians were working at both sites .
Simmons poured 2 small slabs for the condenser units on at each building .
There were 6 sheet rockers working in both Buildings
2 painters were working 1 in each building .
Dellbrook had 1 carpenter working on some misc. carpentry tasks .
The sprinkler company has finished the sprinkler heads and will be installing the turbine next Tuesday .
Weather permitting much of the site work underground should be closed to finish .

William Dillon | 03/23/23 | 05:16PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

2 lifts

William Dillon | 03/23/23 | 05:17PM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/23/23 | 05:17PM

Weather

6:00 AM

45° 

Clear

Wind: 6 MPH | Precipitation: .0" | Humidity: 71%

12:00 PM

49° 

Clear

Wind: 9 MPH | Precipitation: .0" | Humidity: 53%

4:00 PM

53° 

Clear

Wind: 7 MPH | Precipitation: .0" | Humidity: 44%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- Small crew today .
Jim Watt and Mike Leon in for Dellbrook .
2 painters working in EMS.
4 sheet rockers working in Both Buildings .
Mike and Jim were doing a big clean up .
Mike was trying to understand the 2 hour wall separation from the office areas and Decon rooms ,he was going to issue an RFI to get some clarification.
I measured the height of the pipes going across the Apparatus bays in the FH and noted to Jim Watt that the pipes were 9" below the overhead door tracks and will need to be raised .
I also once again showed Jim how drainage around FH needs to be lowered and pulled back to install the perimeter insulation , and meet code regarding distance from grade to siding .

William Dillon | 03/25/23 | 07:17AM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

2 Lifts

William Dillon | 03/25/23 | 07:18AM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/25/23 | 07:18AM

Weather

6:00 AM

25° 

Clear

Wind: 0 MPH | Precipitation: .0" | Humidity: 91%

12:00 PM

44° 

Partially cloudy

Wind: 6 MPH | Precipitation: .0" | Humidity: 65%

4:00 PM

44° 

Partially cloudy

Wind: 8 MPH | Precipitation: .0" | Humidity: 70%

Work Logs




No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Mike Leon onsite for Dellbrook .
3 men from Farland finished digging septic tank hole at EMS and started installing drainage at front of EMS. The crane is coming tomorrow to install tank and Turbine for Sprinklers .
The turbine and associated parts arrived today.
There were 3 electricians working in both buildings wiring all loads into breaker panels.
There were 6 sheet rockers working in the EMS.
The steel erection workers did not show up as expected ,Mike says they will be in tomorrow to fabricate the steel bent . Briggs engineering will be out on Wednesday to X-ray welding . The plan is to X-ray one side and if there is no porosity we will not X-ray the other side.
Marshall Puffer the Structural Engineer is coming on Wednesday to look at structure , if all meets his approval the shoring can be removed and apparatus bay finished .

William Dillon | 03/28/23 | 07:35AM

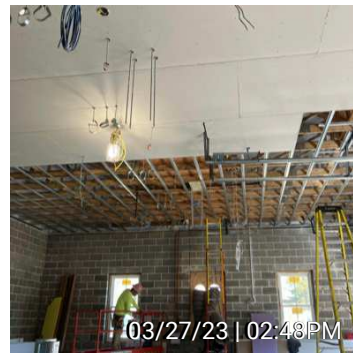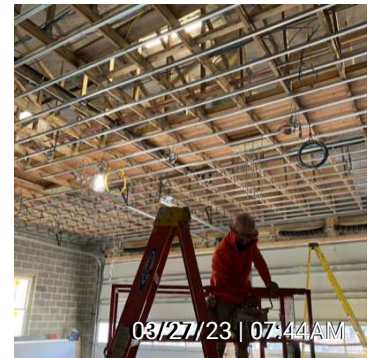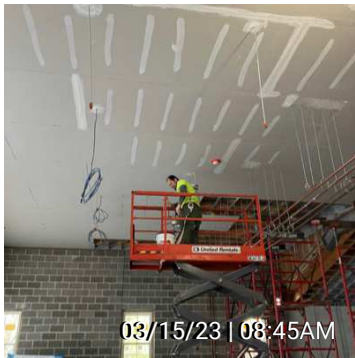

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	2lifts William Dillon 03/28/23 07:33AM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/28/23 | 07:35AM

Weather

6:00 AM

40° 

Overcast

Wind: 7 MPH | Precipitation: .0" | Humidity: 93%

12:00 PM

43° 

Overcast

Wind: 7 MPH | Precipitation: .0" | Humidity: 88%

4:00 PM

45° 

Overcast

Wind: 10 MPH | Precipitation: .0" | Humidity: 80%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Today Mike Leon and Jim Watt were onsite for Dellbrook.
The turbine was lowered through the roof and into the sprinkler room by Baxter crane . Baxter also set the septic tank at the EMS .
There were 4 men from Yankee sprinkler on site .
Farland started pulling Macadam from the front of the FH in order to install tight tanks and drainage structure . I will have to be onsite while the excavation for the tight tanks happens to verify soils .
The steel workers did not show up again ,and Mike says they will be here tomorrow .
The 3 Electricians were still wiring in panels in both buildings .
Mid day the ceiling contractor arrived and started working in the FH .
We should see the plumbers , and tin knockers back tomorrow as well .
I mentioned to Mike Leon that we need to have the ductwork tested as per specs and contract and it should be done before duct insulation .
The 6 sheet rockers were still hanging and taping in both buildings .
William Dillon | 03/28/23 | 05:45PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Mike Leon got a very bad splinter through his finger which required him to go to hospital and have it cut out . <small>William Dillon 03/28/23 05:49PM</small>

2. Any schedule delays occur?

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

2 lifts

William Dillon | 03/28/23 | 05:49PM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/28/23 | 05:50PM

Weather

6:00 AM

32° 

Clear

Wind: 8 MPH | Precipitation: .0" | Humidity: 93%

12:00 PM

47° 

Clear

Wind: 7 MPH | Precipitation: .0" | Humidity: 41%

4:00 PM

47° 

Clear

Wind: 12 MPH | Precipitation: .0" | Humidity: 44%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- Today on site the Dellbrook team was there for the team meeting along with Mike Owen and Adtyai. The schedule was looked over and all the COR logs were looked at as were the RFIs.
In the FH the steel guys had not showed up by 3 so I hope to see them in the AM.
The 3 Electricians have finished both switch gear rooms in both Buildings and have started installing some finish devices in the FH .
The two ceiling installers will be finished with the grid in the FH tomorrow .
The tight tanks were installed in front of the FH without needing to remove unsuitable soils , this could save close to \$28K we will see after its all done . I watched over the entire excavation as did Briggs Engineering and there were no bad soils. Farland had 3 men working.
There was a 12:00 sub contractor meeting with Dellbrook and all subs to make sure all the ducks are in a row as we get closer to finish on both buildings .
There was a 9:00 AM commissioning meeting With all MEP subs and a protocol for start up was started .
At the EMS there were 6 sheet-rockers working and 1 in the FH .
Dellbrook also had 2 Carpenters working on odd jobs on both sites

William Dillon | 03/29/23 | 06:13PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3. Did weather cause any delays?

4. Any visitors on site?

Mike Owen ,John Kenny and Dellbrook team

William Dillon | 03/29/23 | 06:13PM

5. Any areas that can't be worked on?

6. Any equipment rented on site?

2 lifts

William Dillon | 03/29/23 | 06:13PM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/29/23 | 06:13PM

Weather

6:00 AM

35° 

Partially cloudy

Wind: 16 MPH | Precipitation: .0" | Humidity: 50%

12:00 PM

41° 

Clear

Wind: 13 MPH | Precipitation: .0" | Humidity: 27%

4:00 PM

44° 

Clear

Wind: 12 MPH | Precipitation: .0" | Humidity: 22%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0



General Notes

1. Mike Leon and Jim Watt on site for Dellbrook
The 2 tin Knockers were working at the EMS building setting equipment.
The 3 electricians have finished the electric panel work at the FH, and moved up to EMS to be ready for main power startup.
The ceiling grid installers have finished grid in FH, they will come back to finish tile install after all mechanical equip is installed above the grid.
The 5 sheet-rockers have been finishing the MR board and core board at the EMS .
Finally the 3 steel workers are on site fabricating and installing the steel beam fix ,
I left the FH at 5:00 and one beam was up and repaired ,everything must be final welded and ready for Xray test next Tuesday . They told me they will be on site till Saturday afternoon.
Farland had 2 men installing and compacting soil at tight tanks at front of FH

William Dillon | 03/31/23 | 07:41AM

2. Sprinkler turbine install and steel beam repair

William Dillon | 03/31/23 | 07:49AM

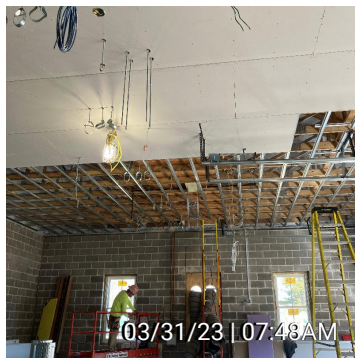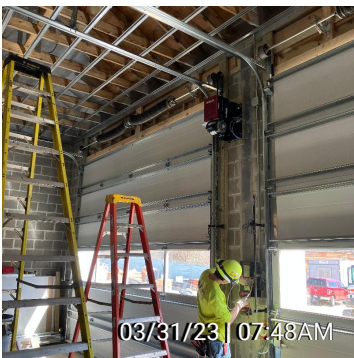



Site Safety Observations No entry

Quality Control Observations No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	2 Lifts William Dillon 03/31/23 07:50AM

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 03/31/23 | 07:50AM
