

Date Mon 10/03/2022

Job #

Prepared By William Dillon

Weather

6:00 AM

50° 

Clear

Wind: 5 MPH | Precipitation: .0" | Humidity: 89%

12:00 PM

78° 

Clear

Wind: 6 MPH | Precipitation: .0" | Humidity: 29%

4:00 PM

85° 

Clear

Wind: 6 MPH | Precipitation: .0" | Humidity: 17%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- The boats from Falmoth did not run ,so the masons and other workers taking those boats did come in 9 carpenters took the SSA and came to work at the FH
Mike Leon came in and had gone home or to a different job by 2pm

William Dillon | 10/03/22 | 01:49PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Safety Officer for True Brother Carpentry William Dillon 10/03/22 01:51PM
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/03/22 | 01:51PM

Date Mon 10/03/2022

Job #

Prepared By William Dillon

Weather

6:00 AM

50° 

Clear

Wind: 5 MPH | Precipitation: .0" | Humidity: 89%

12:00 PM

78° 

Clear

Wind: 6 MPH | Precipitation: .0" | Humidity: 29%

4:00 PM

85° 

Clear

Wind: 6 MPH | Precipitation: .0" | Humidity: 17%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- The boats from Falmoth did not run ,so the masons and other workers taking those boats did come in 9 carpenters took the SSA and came to work at the FH
Mike Leon came in and had gone home or to a different job by 2pm

William Dillon | 10/03/22 | 01:49PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Safety Officer for True Brother Carpentry William Dillon 10/03/22 01:51PM
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/03/22 | 01:51PM

Date Wed 10/05/2022

Job #

Prepared By William Dillon

Weather

6:00 AM

56° 

Partly Cloudy

Wind: 5 MPH | Precipitation: .0" | Humidity: 73%

12:00 PM

77° 

Mostly Cloudy

Wind: 8 MPH | Precipitation: .0" | Humidity: 40%

4:00 PM

85° 

Partly Cloudy

Wind: 9 MPH | Precipitation: .0" | Humidity: 28%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Full team meeting with John Kenny ,Antonia ,Micheal Owen ,Full Dellbrook team
Mike Leon went over Schedule and critical paths . White Cedar Shingles are still and issue and may not be available till January
On site today were 1 Electrician , 6 Masons , Mike Leon and Jim Watt
The siren location was discussed and site chosen just outside the EMS parking area between the FH and EMS
The discussion regarding the grading was solved as Reids drawings were spot on .
after the building committee meeting Mike Owen and I resolved the grading issues between the FH and TH
William Dillon | 10/05/22 | 01:48PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	yes the carpenters lost yesterday and today due to rain and wind <small>William Dillon 10/05/22 01:49PM</small>
4. Any visitors on site?				Dellbrook team ,Mike Owen , John

Kenny and Antonia
William Dillon | 10/05/22 | 01:50PM

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/05/22 | 01:50PM

Weather

6:00 AM

60° 

Overcast

Wind: 15 MPH | Precipitation: .06" | Humidity: 92%

12:00 PM

62° 

Mostly Cloudy

Wind: 11 MPH | Precipitation: .06" | Humidity: 87%

4:00 PM

63° 

Mostly Cloudy

Wind: 6 MPH | Precipitation: .06" | Humidity: 83%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Mike Leon and Jim Watt on site .Mike Left at 11 for appointment
1 electrician on site
6 Carpenters working at FH
6 Masons at EMS finishing out side CMU walls They hope to finish up at EMS next week then move down to FH
I discussed missing blocking at Fire house and Jim said he would make sure that it gets done .

William Dillon | 10/06/22 | 01:36PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/06/22 | 01:37PM

Weather

6:00 AM

62° 

Clear

Wind: 9 MPH | Precipitation: .0" | Humidity: 91%

12:00 PM

64° 

Clear

Wind: 13 MPH | Precipitation: .0" | Humidity: 89%

4:00 PM

64° 

Clear

Wind: 15 MPH | Precipitation: .0" | Humidity: 86%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Mike Leon and Jim Watt onsite for Dellbrook

I called Cottles and inquired about buying white Cedar Shingles . They told me they get a load every few weeks. If we had a place to store them they would give us a pallet every few weeks since we won't need them till January . That way Dellbrook can start warehousing shingles till they are needed . Then Dellbrook can look at other sources at the same time .

6 masons on site at EMS

5 Carpenters on site at FH

William Dillon | 10/07/22 | 05:54PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/07/22 | 05:54PM

Weather

6:00 AM

57° 

Clear

Wind: 5 MPH | Precipitation: .01" | Humidity: 85%

12:00 PM

61° 

Clear

Wind: 5 MPH | Precipitation: .01" | Humidity: 69%

4:00 PM

61° 

Clear

Wind: 8 MPH | Precipitation: .01" | Humidity: 65%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Mike Leon , and Jim Watt in for Dellbrook
6 masons finishing walls at EMS starting to break down scaffolding
1 electrician working both sites
5 carpenters doing fireproof walls at FH and installing joist hangers
The carpenters are waterproofing the roof area over the Electron at FH so Duct bank can be installed

William Dillon | 10/11/22 | 12:58PM

Site Safety Observations

1. Mike Leon has arranged for a company that is safety experts to come on the 17th to oversee the silo and tank leak investigation

William Dillon | 10/11/22 | 12:59PM

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/11/22 | 12:59PM

Date Tue 10/11/2022

Job #

Prepared By William Dillon

Weather

6:00 AM

57° 

Clear

Wind: 5 MPH | Precipitation: .01" | Humidity: 85%

12:00 PM

61° 

Clear

Wind: 5 MPH | Precipitation: .01" | Humidity: 69%

4:00 PM

61° 

Clear

Wind: 8 MPH | Precipitation: .01" | Humidity: 65%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Mike Leon , and Jim Watt in for Dellbrook
6 masons finishing walls at EMS starting to break down scaffolding
1 electrician working both sites
5 carpenters doing fireproof walls at FH and installing joist hangers
The carpenters are waterproofing the roof area over the Electron at FH so Duct bank can be installed

William Dillon | 10/11/22 | 12:58PM

Site Safety Observations

1. Mike Leon has arranged for a company that is safety experts to come on the 17th to oversee the silo and tank leak investigation

William Dillon | 10/11/22 | 12:59PM

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/11/22 | 12:59PM

Weather

6:00 AM

63° 

Mostly Cloudy

Wind: 20 MPH | Precipitation: .0" | Humidity: 87%

12:00 PM

64° 

Mostly Cloudy

Wind: 23 MPH | Precipitation: .0" | Humidity: 80%

4:00 PM

64° 

Overcast

Wind: 22 MPH | Precipitation: .01" | Humidity: 83%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

No entry

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Date Fri 10/14/2022

Job #

Prepared By William Dillon

Weather

6:00 AM

64° 

Rain

Wind: 25 MPH | Precipitation: .7" | Humidity: 98%

12:00 PM

63° 

Overcast

Wind: 22 MPH | Precipitation: .99" | Humidity: 94%

4:00 PM

63° 

Mostly Cloudy

Wind: 10 MPH | Precipitation: 1.01" | Humidity: 87%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Mike Leon contacted me to say that no one would be on site today because of the boats not running

William Dillon | 10/14/22 | 07:55AM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	no boats running so no one on site working William Dillon 10/14/22 07:56AM
3. Did weather cause any delays?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Boats did not ru William Dillon 10/14/22 07:56AM
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/14/22 | 07:57AM

Weather

6:00 AM

58° 

Overcast

Wind: 5 MPH | Precipitation: .0" | Humidity: 70%

12:00 PM

63° 

Overcast

Wind: 13 MPH | Precipitation: .02" | Humidity: 69%

4:00 PM

63° 

Possible Light Rain

Wind: 18 MPH | Precipitation: .07" | Humidity: 74%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Today Mike Leon and Jim watt onsite for Dellbrook
There were 6 Carpenters working at FH , starting the porch at the parking area .
There were 6 masons on site working at EMS
There were 2 men from Farland working on site clean up and trench prep for electricity to EMS , Farland and the Masons moved the trusses from the FH parking area to the EMS freeing up area for the coming trench to bring power to FH
There were two electricians working on both sites one setting boxes in Electric room at FH and one setting boxes in CMU walls at EMS
Mike Leon informed me that the safety plan for entering the tank and Silo has not been approved as of this morning .
We also noticed that the insulation that was delivered is not what was in submittals so that will be returned and the proper insulation board bought and installed .
I stopped at Reids office and asked him to please get rim high and inverts done before the Wednesday Team meeting . Reid agreed to get it done this afternoon .
The next Two weeks will be critical to the job moving ahead on schedule , lots of moving parts and lots of trades involved

William Dillon | 10/17/22 | 05:51PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

2. Any schedule delays occur?

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/17/22 | 05:51PM

Weather

6:00 AM

62° 

Possible Light Rain

Wind: 11 MPH | Precipitation: .39" | Humidity: 83%

12:00 PM

63° 

Partly Cloudy

Wind: 14 MPH | Precipitation: .44" | Humidity: 79%

4:00 PM

60° 

Clear

Wind: 16 MPH | Precipitation: .44" | Humidity: 63%

Work Logs


No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- No Carpenters on site at FH
 6 masons working at EMS on interior walls
 2 men from Farland starting trenching for power at both sites
 Mike Leon said insulation was ordered wrong we will discuss at Wednesdays team meeting
 Simmons concrete had one man working on slab detailing at EMS see Pictures

William Dillon | 10/18/22 | 03:29PM

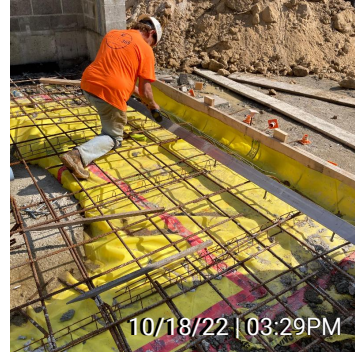

- Mike Leon called for a Partial inspection for the electric room at the FH I told him to take pictures of Room and all walls and we would figure out what to do

William Dillon | 10/18/22 | 03:41PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
-----------	-----	----	-----	-------------

1. Any accidents on site today?

2. Any schedule delays occur?

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/18/22 | 03:41PM

Weather

6:00 AM

54° 

Clear

Wind: 16 MPH | Precipitation: .0" | Humidity: 64%

12:00 PM

55° 

Clear

Wind: 19 MPH | Precipitation: .0" | Humidity: 56%

4:00 PM

55° 

Clear

Wind: 19 MPH | Precipitation: .0" | Humidity: 55%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

No entry

Site Safety Observations

- lab poured with angle irons at EMS I checked with plumber that trench drain was still correct
3 men from Simmons pouring slab with Pump truck
6 masons working on interior CMU walls at EMS
4 carpenters working at FH
Team meeting with Dellbrook Mike Owen and his team Adti , and Basil and John Kenny
Mike Leon and I will inspect nailing at shear walls
Jim Watt also on site and he will be watching Job until Mike gets back next Tuesday
2 electricians workin at both sites on Duct banks with women from Farland

William Dillon | 10/19/22 | 02:40PM

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/19/22 | 02:40PM

Date Thu 10/20/2022

Job #

Prepared By William Dillon

Weather

6:00 AM

54° 

Partly Cloudy

Wind: 19 MPH | Precipitation: .01" | Humidity: 59%

12:00 PM

56° 

Clear

Wind: 21 MPH | Precipitation: .01" | Humidity: 58%

4:00 PM

57° 

Clear

Wind: 21 MPH | Precipitation: .01" | Humidity: 54%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- 4 Carpenters working on back porch of FH
2 men from Farland trenching for power at EMS trench was dug out past job trailer and covered with concrete
conduit installed by American Electric including temp power direct burial cable to temp service 1 electrician
6 masons still working on interior walls at EMS

William Dillon | 10/20/22 | 03:16PM



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
-----------	-----	----	-----	-------------

- Any accidents on site today?

2. Any schedule delays occur?

3. Did weather cause any delays?

4. Any visitors on site?

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/20/22 | 03:16PM

Weather

6:00 AM

57° 

Partly Cloudy

Wind: 12 MPH | Precipitation: .0" | Humidity: 58%

12:00 PM

61° 

Clear

Wind: 9 MPH | Precipitation: .01" | Humidity: 49%

4:00 PM

61° 

Clear

Wind: 15 MPH | Precipitation: .01" | Humidity: 54%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Jim Watt on site for Dellbrook
Two men from Farland onsite finishing concrete in trench at EMS
One man at EMS cutting concrete from Simmons
William Dillon | 10/21/22 | 12:24PM
2. There is a problem with the steel in FH Which John Kenny said he saw in Aditi'S report John called Bill Rossi and said we all talked about the steel and agreed not to talk about it . That did not happen neither Mike Owen or I heard anything about the steel
William Dillon | 10/24/22 | 09:00AM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/24/22 | 09:00AM

Date Mon 10/24/2022

Job #

Prepared By William Dillon

Weather

6:00 AM

60° 

Overcast

Wind: 12 MPH | Precipitation: .11" | Humidity: 88%

12:00 PM

61° 

Overcast

Wind: 10 MPH | Precipitation: .26" | Humidity: 91%

4:00 PM

62° 

Overcast

Wind: 9 MPH | Precipitation: .36" | Humidity: 88%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. I was on site at 8AM and met Jim Watt from Dellbrook ,we went over measurments on the steel and found some problems ,
When I went back in the afternoon Jimsaid his big project manager was on site and they had reviewed plans and submittals along with shop drawings for steel . There seem to be some incosistences which will be reconciled in the next few days .
William Dillon | 10/24/22 | 07:14PM

2. only 2 electricians on site to day because of rain
William Dillon | 10/24/22 | 07:15PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	rain kept carpenters and Masons of site <small>William Dillon 10/24/22 07:15PM</small>
3. Did weather cause any delays?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	same as above <small>William Dillon 10/24/22 07:16PM</small>
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5. Any areas that can't be worked on?

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/24/22 | 07:16PM

Weather

6:00 AM

63° 

Overcast

Wind: 8 MPH | Precipitation: .0" | Humidity: 87%

12:00 PM

63° 

Overcast

Wind: 9 MPH | Precipitation: .01" | Humidity: 86%

4:00 PM

63° 

Foggy

Wind: 10 MPH | Precipitation: .03" | Humidity: 85%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Mike owen and Jim Watt onsite for Dellbrook I spent an hour going over the steel situation and Mike says that we can all talk about what's going to happen in the team meeting tomorrow
6 masons working at the EMS2 electricians working at both sites
more masonry materials delivered to site

William Dillon | 10/25/22 | 02:14PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/25/22 | 02:14PM

Weather

6:00 AM

62° 

Rain

Wind: 8 MPH | Precipitation: .11" | Humidity: 100%

12:00 PM

63° 

Possible Light Rain

Wind: 7 MPH | Precipitation: .35" | Humidity: 100%

4:00 PM

64° 

Mostly Cloudy

Wind: 5 MPH | Precipitation: .36" | Humidity: 100%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Team meeting with Dellbrook ,Tim Carroll ,Bill Rossi, Fire chief ,Michael Owen, Atdai Modi
Masons back on site but let in the morning no other workers onsite

William Dillon | 10/27/22 | 03:33PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Rain sent Masons home William Dillon 10/27/22 03:34PM
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/27/22 | 04:01PM

Weather

6:00 AM

62° 

Partly Cloudy

Wind: 13 MPH | Precipitation: .01" | Humidity: 97%

12:00 PM

63° 

Clear

Wind: 13 MPH | Precipitation: .01" | Humidity: 84%

4:00 PM

64° 

Clear

Wind: 15 MPH | Precipitation: .01" | Humidity: 72%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. True Brothers working framing walls with 4 men at EMS
6 masons working at EMS
1 electrician working at EMS
Mike Leon tells me that Dellbrook is meeting at K and K's office tomorrow to hash out steel issues
William Dillon | 10/27/22 | 03:28PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/27/22 | 03:28PM

Date Fri 10/28/2022

Job #

Prepared By William Dillon

Weather

6:00 AM

53° 

Clear

Wind: 24 MPH | Precipitation: .0" | Humidity: 71%

12:00 PM

55° 

Partly Cloudy

Wind: 22 MPH | Precipitation: .0" | Humidity: 66%

4:00 PM

55° 

Mostly Cloudy

Wind: 20 MPH | Precipitation: .0" | Humidity: 67%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. Mike Owen and Jim Watt onsite
Masons rained out carpenters worked on EMS walls for part of the day
William Dillon | 10/31/22 | 01:16PM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	masons lost the day <small>William Dillon 10/31/22 01:16PM</small>
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

6. Any equipment rented on site?

W D

I, William Dillon, have reviewed and completed this report.

William Dillon | 10/31/22 | 01:16PM
